Project Schedule and Gantt charts made using MS project

GANTT CHART

	Task Name	%	Duration	Finish	Start	Resource Names
1	**1 Project Alpha**	**39%**	**244 days**	**Thu 3/24/16**	**Mon 4/20/15**	
2	**1.1 Business Case**	**64%**	**20 days**	**Fri 5/15/15**	**Mon 4/20/15**	
3	1.1.1 High Level Requirements	100%	10 days	Fri 5/1/15	Mon 4/20/15	SME,Architect,Business Analyst
4	1.1.2 Estimation	40%	5 days	Fri 5/8/15	Mon 5/4/15	Business Analyst,Developer,QA Tester
5	1.1.3 Draft Business Case	40%	10 days	Fri 5/15/15	Mon 5/4/15	Project Manager
6	**1.2 Analysis**	**75%**	**28 days**	**Wed 6/24/15**	**Mon 5/18/15**	
7	1.2.1 Requirement Gathering	30%	10 days	Fri 5/29/15	Mon 5/18/15	Business Analyst
8	1.2.2 Draft Requirements Docur	100%	15 days	Fri 6/19/15	Mon 6/1/15	Business Analyst
9	1.2.3 Requirements Review	100%	2 days	Tue 6/23/15	Mon 6/22/15	Business Analyst,SME,Developer,QA Tester,
10	1.2.4 Requirements Sign-off	100%	1 day	Wed 6/24/15	Wed 6/24/15	SME
11	**1.3 Design**	**89%**	**35 days**	**Wed 8/12/15**	**Thu 6/25/15**	
12	1.3.1 High Level Design Docume	100%	15 days	Wed 7/15/15	Thu 6/25/15	Architect
13	1.3.2 Design Review	80%	20 days	Wed 8/12/15	Thu 7/16/15	Architect,Developer,QA Tester
14	**1.4 Build**	**45%**	**76 days**	**Thu 11/26/15**	**Thu 8/13/15**	
15	**1.4.1 Component 1**	**41%**	**70 days**	**Wed 11/18/15**	**Thu 8/13/15**	
16	1.4.1.1 Sub Component	71%	40 days	Wed 10/7/15	Thu 8/13/15	Developer
17	1.4.1.2 Unit Testing	0%	30 days	Wed 11/18/15	Thu 10/8/15	Developer
18	**1.4.2 Component 2**	**57%**	**50 days**	**Wed 10/21/15**	**Thu 8/13/15**	
19	1.4.2.1 Sub Component	100%	20 days	Wed 9/9/15	Thu 8/13/15	Developer
20	1.4.2.2 Unit Testing	28%	30 days	Wed 10/21/15	Thu 9/10/15	Developer
21	1.4.3 Integration Testing	0%	5 days	Wed 11/25/15	Thu 11/19/15	
22	1.4.4 Configure QA Environmen	0%	1 day	Thu 11/26/15	Thu 11/26/15	Developer
23	**1.5 Quality Assurance Library**	**55%**	**21 days**	**Thu 7/23/15**	**Thu 6/25/15**	
24	1.5.1 Requirement Analysis	100%	5 days	Wed 7/1/15	Thu 6/25/15	QA Tester

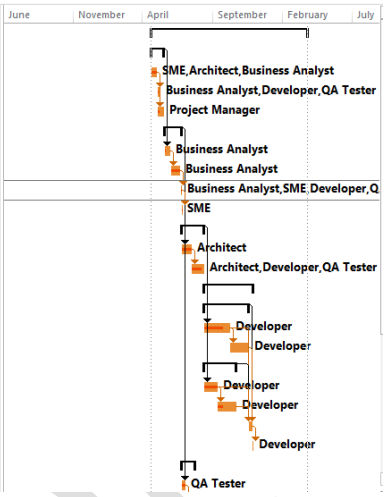

WritingSOL
